Corrin 2028 adds $104m of EBITDA and releases $146m of working capital by FY2028; the board is asked to approve the programme, two plant exits and the $165m it costs

Three approvals asked of the board

1. **Programme.** Approve Corrin 2028 and the $165m to deliver it: $98m of one-off cost and $67m of capital, $72m of it in 2026.
2. **Footprint.** Approve the exits of Salt Lake City by September 2027 and Tuttlingen by June 2028, subject to consultation.
3. **Operating model.** Approve a shared-services hub in Brno, global procurement, and quality and regulatory reporting to the CEO.

If approved, the programme launches in January 2026 at M1, and the board reviews it at each of five further milestones to December 2028.

What it costs and when it pays back

$m	2026	2027	2028	Total
One-off operating cost	44	36	18	98
Capital expenditure	28	25	14	67
Cost to achieve	**72**	**61**	**32**	**165**
Net cash after cost	(16)	52	99	135
Cumulative net cash	**(16)**	**36**	**135**	

Cash turns positive in 2027 because working capital is released ahead of the full run-rate.

In this pack

Page	What it proves
2	Order to cash: 70 days today, six pain points costing $28m a year
3	Footprint: seven plants become five; utilisation from 64% to 84%
4	Prioritisation: fourteen initiatives on value, ease and cost
5	Value bridge: $186m to $290m of EBITDA, and the cash case
6	Roadmap: 2026 to 2028, six milestones, three dependencies
7	Operating model: five new units, two fewer layers
8	Risks: nine scored before and after mitigation

Eight commitments for FY2028

FY2028 target in petrol and its change from the FY2025 baseline; bars show FY2025, the FY2026 and FY2027 interim targets and FY2028 on one scale; the page that proves each, top right

Run-rate EBITDA — p. 5

$290m

+$104m from $186m

FY25	$186m
FY26	$217m
FY27	$256m
FY28	$290m

$103m from four levers and $38m from volume, less $37m of inflation and run costs

Owner: CFO
Initiatives: all twelve

EBITDA margin — p. 5

20%

+5 pts from 15%

FY25	15%
FY26	17%
FY27	19%
FY28	20%

EBITDA grows faster than revenue, which rises 5.4% a year to $1,450m

Owner: CFO
Initiatives: all twelve

Order-to-cash days — p. 2

51

-19 days from 70

FY25	70
FY26	64
FY27	57
FY28	51

Avoidable delay falls from 25 to 6 days, releasing $75m of receivables

Owner: CFO
Initiatives: C1 to C3, O1

Inventory days — p. 5

105

-37 days from 142

FY25	142
FY26	131
FY27	117
FY28	105

One global plan across five plants releases $71m of stock

Owner: COO
Initiatives: F3, planning

On time, in full — p. 6

96%

+9 pts from 87%

FY25	87%
FY26	90%
FY27	93%
FY28	96%

One global supply chain; lines dual-qualified before each move

Owner: COO
Initiatives: F1 to F3

Network utilisation — p. 3

84%

+20 pts from 64%

FY25	64%
FY26	67%
FY27	76%
FY28	84%

Steps up in 2027 as Salt Lake City closes, and again with Tuttlingen

Owner: COO
Initiatives: F1, F2

Invoice lines priced right — p. 2

99.5%

+6.7 pts from 92.8%

FY25	92.8%
FY26	96.5%
FY27	98.8%
FY28	99.5%

One contract-price master replaces 12 hand-kept GPO price lists

Owner: CCO
Initiatives: C1

G&A cost, % of revenue — p. 7

9.4%

-2.2 pts from 11.6%

FY25	11.6%
FY26	11.1%
FY27	10.2%
FY28	9.4%

Brno hub, 190 fewer G&A roles and two fewer management layers

Owner: CFO
Initiatives: O1, O2

Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

Order-to-cash takes 70 days, 25 beyond contract terms; six pain points cost $28m a year

The cycle today: seven steps, 70 days from order to cash, 58.8 of them in Collect

Average days per order and the share of orders handled by hand at each step; FY2028 target in petrol; the dominant step in orange

1 Capture order → 2 Price and credit → 3 Allocate and pick → 4 Ship, confirm use → 5 Invoice → **6 Collect** → 7 Apply cash

Per order	1	2	3	4	5	6	7
Days, FY2025	0.9	1.6	1.2	3.1	2.4	58.8	2.0
Days, FY2028 target	**0.2**	**0.3**	**0.8**	**1.6**	**0.2**	**47.5**	**0.4**
Handled by hand, FY2025	41%	36%	22%	30%	18%	25%	28%
Handled by hand, FY2028	**10%**	**8%**	**15%**	**12%**	**3%**	**8%**	**6%**


Six pain points cost $28m a year

Numbers match the orange marks on the flow; cost is annual leakage, rework and write-off

#	Step	Pain point and evidence	$m a year	Fixed by
1	1 Capture order	41% of orders arrive by fax or e-mail and are re-keyed; 3.8% carry an entry error	3.1	O1, C1
2	2 Price and credit	12 GPO price lists kept by hand; 7.2% of invoice lines priced wrong	**14.6**	C1
3	4 Ship, confirm use	Bill-only implant use reported 9.0 days after surgery; consignment counted by hand	2.8	C2
4	5 Invoice	Invoices issued 2.4 days after shipment; 18% need a manual release	1.2	O1
5	6 Collect	9.4% of invoices disputed, 34 days to resolve: 13.8 days past terms	4.9	C3
6	7 Apply cash	28% of remittances matched to invoices by hand	1.4	C3
	Total		**28.0**	

Where the 70 days go

Average days from order to cash: pale, contract terms, unchanged; orange, avoidable delay

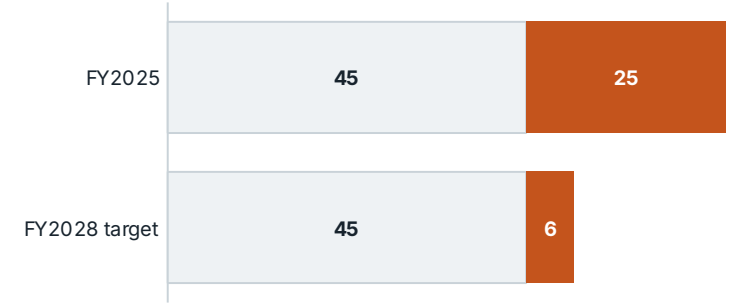

Avoidable days, by where they arise	FY2025	FY2028
Collect past contract terms, step 6	13.8	**2.5**
Processing in the other six steps	11.2	**3.5**
Avoidable delay	**25.0**	**6.0**

Cutting 19 avoidable days releases $75m of receivables at FY2028 revenue. The C initiatives capture $18m of the $28m a year, 64%.

Four initiatives remove them

C1 Contract-price master
$10m run-rate for $7m; live in the US in May 2026; fixes pain point 2 and the pricing half of 1

C2 Bill-only digitised
$4m for $8m; surgeons' implant use reported from the theatre on the day of surgery: pain point 3

C3 Collections automation
$4m for $6m; disputes routed by cause and cash matched by rule: pain points 5 and 6

O1 Brno hub
Order entry and invoicing move to one team in January 2027, removing the re-keying in pain points 1 and 4


Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

FOOTPRINT | SEVEN PLANTS TO FIVE

Two plant exits lift network utilisation from 64% to 84% and save $29m a year

Two regional clusters, two closures, three line transfers

Each closing plant's lines go to the nearest plant that already makes or services the product

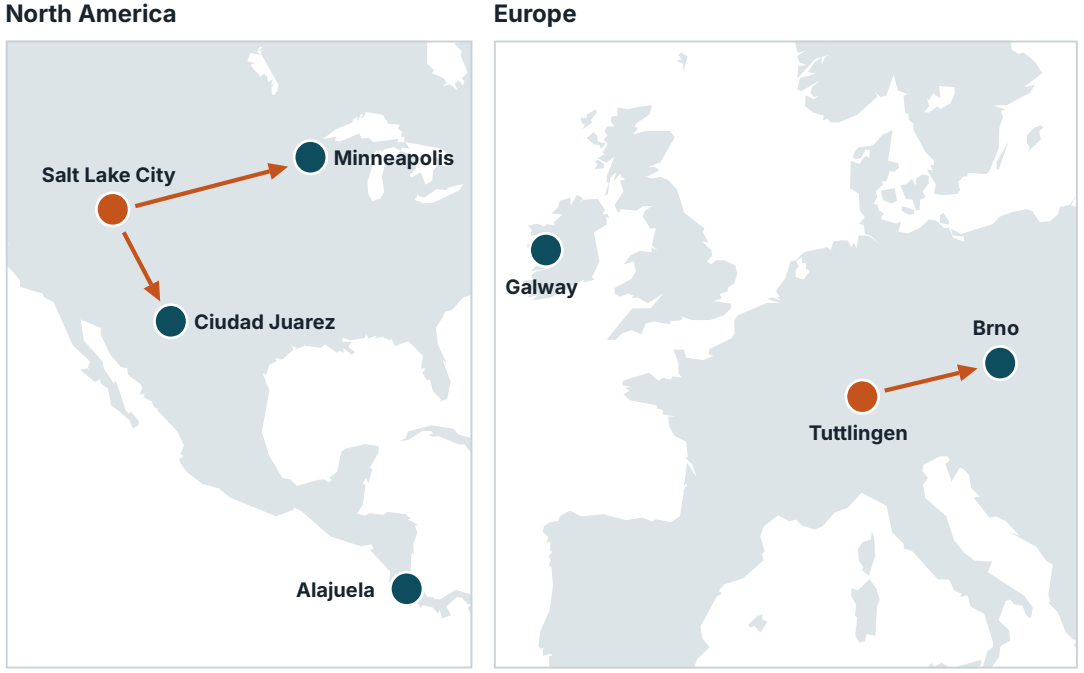

Salt Lake City's pump electronics move to Minneapolis and its infusion sets to Ciudad Juarez; Tuttlingen's instruments move 590 km to Brno, which already reprocesses them.

84%
Network utilisation in FY2028, capacity-weighted, from 64%

9 lines
Moved in three transfers, one at a time, by June 2028

-150
Net headcount: 4,020 to 3,870, as receiving plants hire 550

Capacity, utilisation and headcount by plant

Capacity is annual output at standard cost; utilisation is output over capacity; FY2028 in petrol, closing plants in orange

		Capacity, $m		Utilisation, %		Headcount		
Plant	**Products**	**FY25**	**FY28**	**FY25**	**FY28**	**FY25**	**FY28**	**Action**
Minneapolis	Monitoring systems	260	**290**	66	**86**	640	**760**	Expand: pump electronics
Salt Lake City	Infusion pumps	150	-	48	-	410	-	Exit by September 2027
Ciudad Juarez	Infusion sets	300	**360**	79	**88**	980	**1,150**	Expand: infusion sets
Alajuela	Catheters	210	**210**	70	**81**	720	**760**	Retain
Galway	EU sterile catheters	190	**190**	66	**78**	530	**560**	Retain
Tuttlingen	Surgical instruments	110	-	41	-	290	-	Exit by June 2028
Brno	Reprocessing	160	**200**	52	**80**	450	**640**	Expand: instruments
Network	**Seven plants to five**	**1,380**	**1,250**	**64**	**84**	**4,020**	**3,870**	

Capacity falls by $130m to $1,250m: the network loses its two least-used plants, at 48% and 41%, and fills the rest.

Three line transfers, one at a time

Lines moved	From	To	Validation	Cut-over
Pump electronics, 2 lines	Salt Lake City	Minneapolis	Jan to Apr 2027	June 2027
Infusion sets, 3 lines	Salt Lake City	Ciudad Juarez	Mar to Jul 2027	September 2027
Surgical instruments, 4 lines	Tuttlingen	Brno	Oct 2027 to Mar 2028	June 2028

Each line runs 10 to 12 weeks of bridge stock through its cut-over; validation is re-qualification under the receiving plant's quality system.

The $29m saving pays back the $68m in 2.3 years

Footprint initiative	Run-rate saving, $m	One-off cost, $m	Payback, years
F1 Salt Lake City exit	**15**	38	2.5
F2 Tuttlingen exit to Brno	**9**	24	2.7
F3 Lean and OEE in retained plants	**5**	6	1.2
Footprint lever	**29**	**68**	**2.3**


Payback is one-off cost and capital over the run-rate saving; F1's saving starts at M4 in September 2027 and F2's at M5 in June 2028.

Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

Four strategic bets hold 46% of the value and 64% of the cost; two quick wins start now

Value against ease of delivery, sized by cost

Each point is one initiative by code: strategic bets in orange, other initiatives in petrol, deferred ideas in grey

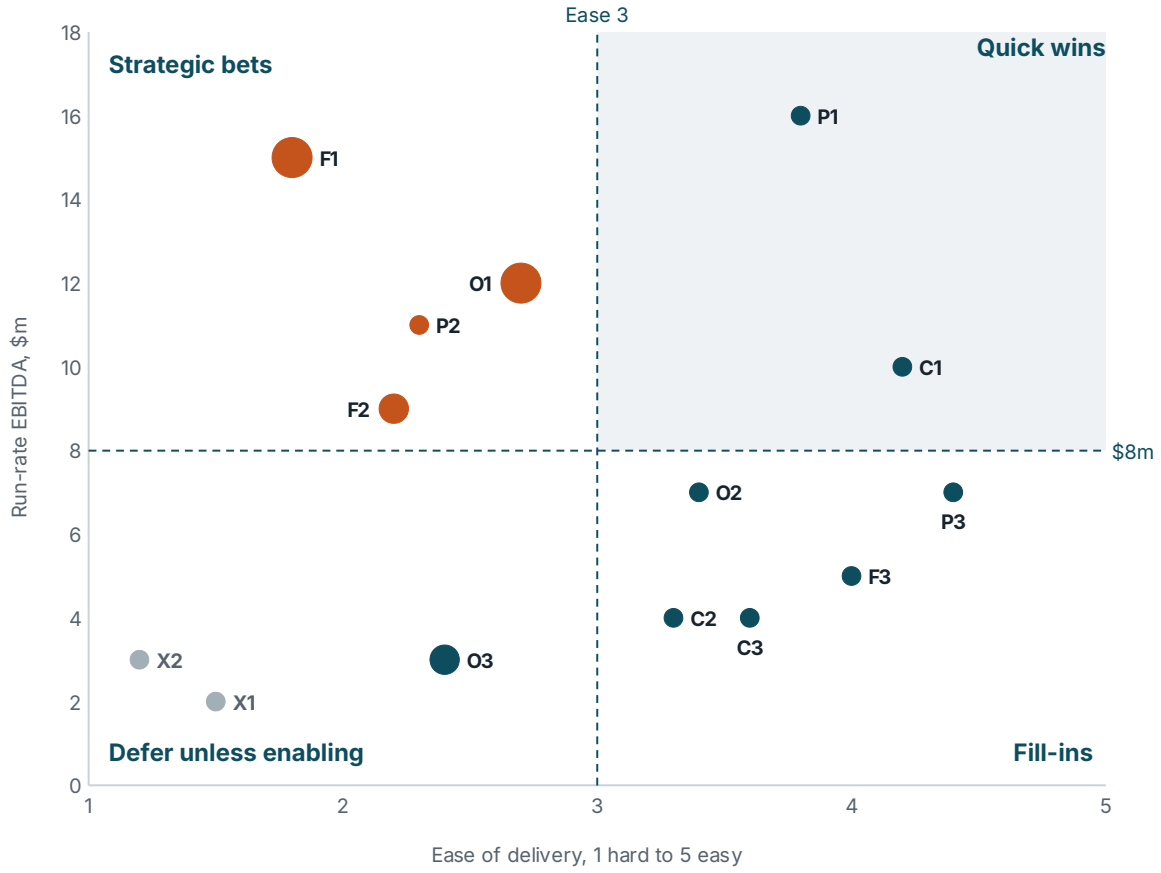

Marker size is the cost to achieve: under $10m · $10m to $25m · over $25m

Twelve initiatives in the plan

Run-rate EBITDA and cost to achieve, $m; ease scored 1 hard to 5 easy; strategic bets in orange

Code	Initiative	$m EBITDA	$m cost	Ease	Quadrant	Wave
P1	Direct-material re-sourcing	16	6	3.8	Quick win	1
P2	BOM value engineering, top 20 SKUs	11	9	2.3	Strategic bet	2
P3	Indirect spend and freight tender	7	2	4.4	Fill-in	1
F1	Salt Lake City exit	15	38	1.8	Strategic bet	2
F2	Tuttlingen exit to Brno	9	24	2.2	Strategic bet	3
F3	Lean and OEE in retained plants	5	6	4.0	Fill-in	1
C1	Contract-price master, GPO compliance	10	7	4.2	Quick win	1
C2	Bill-only and consignment digitised	4	8	3.3	Fill-in	2
C3	Collections and dispute automation	4	6	3.6	Fill-in	1
O1	Shared-services hub, Brno	12	34	2.7	Strategic bet	2
O2	Spans and layers, commercial and G&A	7	9	3.4	Fill-in	1
O3	Global quality and regulatory function	3	16	2.4	Enabler	1
	Total, twelve initiatives	**103**	**165**			

The four strategic bets, P2, F1, F2 and O1, carry $47m of the $103m, 46%, and $105m of the $165m cost, 64%: they are where delivery risk sits.

The quick wins, P1 and C1, add $26m for $13m and start in January 2026. Wave 1 is seven initiatives worth $52m for $52m of cost, all started by April 2026.

Deferred: X1 own distribution in DACH ($2m, ease 1.5) and X2 single-step ERP replacement ($3m, ease 1.2).

By lever: what each dollar of EBITDA costs


Lever	$m EBITDA	$m cost	Cost per $ of EBITDA
Procurement, P1 to P3	34	17	0.50
Footprint, F1 to F3	29	68	2.34
Commercial and order to cash, C1 to C3	18	21	1.17
Operating model, O1 to O3	22	59	2.68
Total	**103**	**165**	

Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

Volume offsets inflation and run costs; four levers add $103m, taking EBITDA to $290m

FY2025 EBITDA to FY2028 exit run-rate, $m

Totals in dark petrol, increases in mid petrol, decreases in grey; volume first nets off inflation and run costs; cost to achieve under each lever

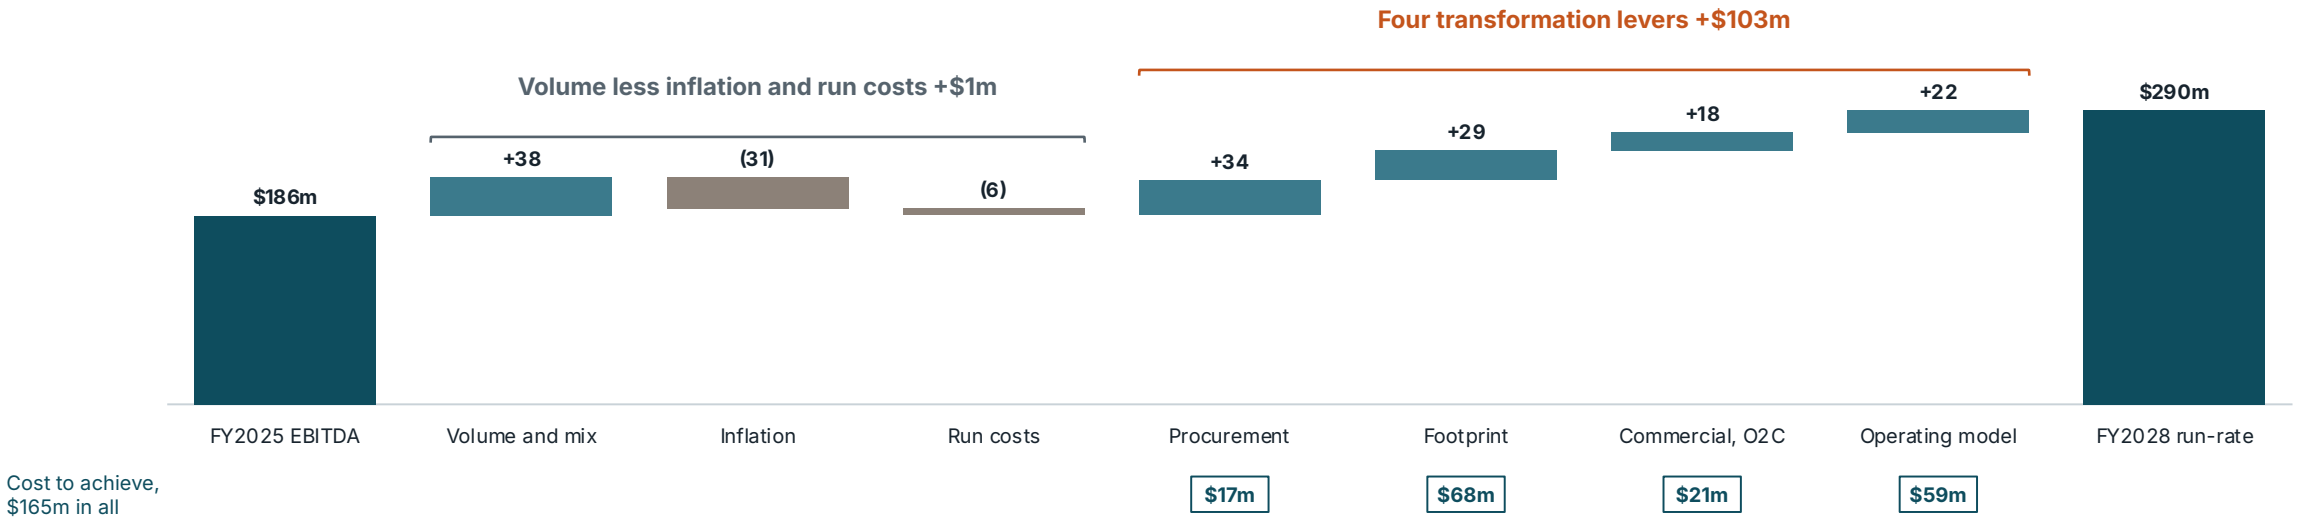

EBITDA builds over three years

Run-rate at each year end, $m; margin on that year's revenue

$m, run-rate at year end	2025	2026	2027	2028
Revenue	1,240	1,310	1,380	1,450
EBITDA at FY2025	186	186	186	186
Volume and mix		12	25	38
Inflation		(10)	(21)	(31)
Run costs		(3)	(5)	(6)
Transformation levers		32	71	103
Run-rate EBITDA	**186**	**217**	**256**	**290**
EBITDA margin, %	*15.0*	*16.6*	*18.6*	*20.0*

Cash turns positive in 2027

In-year savings as phased in the benefit plan, $m

$m, in year	2026	2027	2028	Total
In-year savings	16	51	87	154
Working capital released	40	62	44	146
One-off operating cost	(44)	(36)	(18)	(98)
Capital expenditure	(28)	(25)	(14)	(67)
Net cash	**(16)**	**52**	**99**	**135**
Cumulative net cash	**(16)**	**36**	**135**	

What the bridge assumes

- Volume and mix: revenue grows 5.4% a year to $1,450m on the current portfolio, with no new launches.
- Inflation: wages 3.5% and materials 2.5% a year, offset only where index clauses apply.
- Run costs: $6m a year for the planning system, the hub's licences and the quality function.
- Working capital: $75m from receivables and $71m from inventory, at FY2028 revenue and cost.
- Cost to achieve: $165m, $98m of it one-off operating cost and $67m capital; 44% falls in 2026.


Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

ROADMAP | 2026 TO 2028

Seven initiatives start by April 2026; the two plant exits run back to back to June 2028

Twelve initiatives, January 2026 to December 2028, in order of start

Light petrol: design; petrol: delivery to full run-rate; orange diamonds: milestones; right: deliveries that wait for another initiative or a milestone

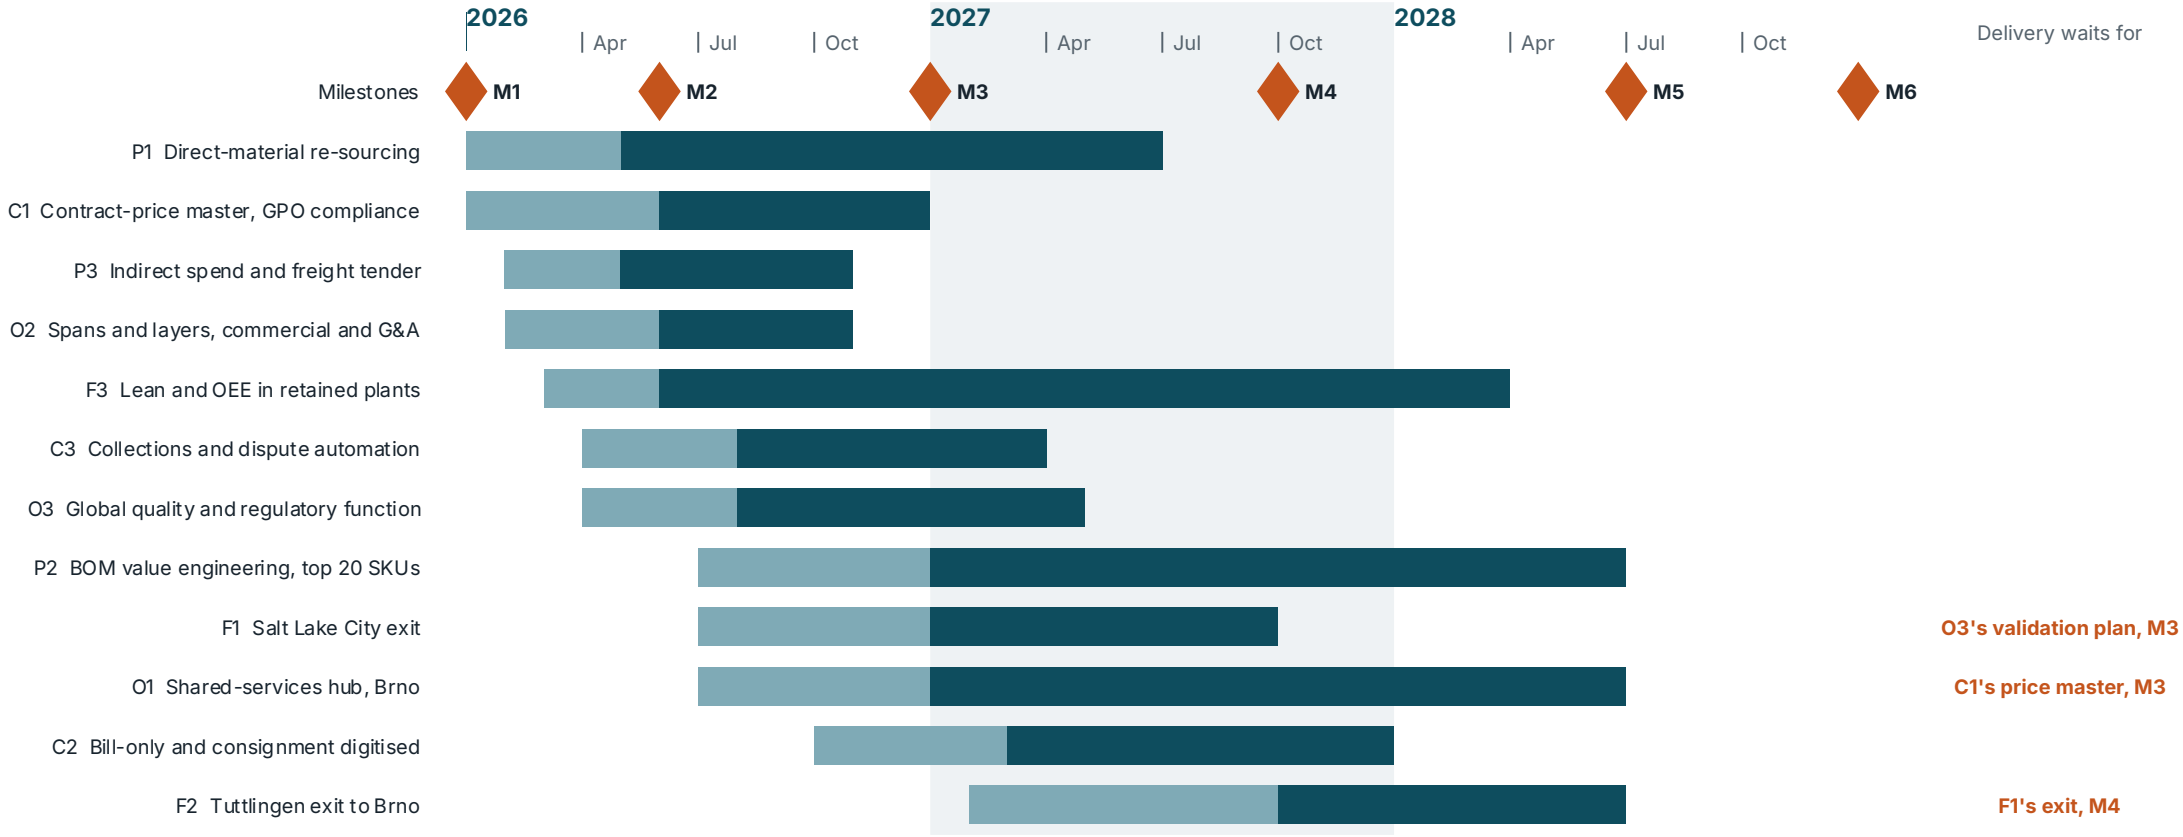

Milestones the board will see reported

M1 January 2026
Programme launch; Transformation Office live

M2 May 2026
Contract-price master live in the US

M3 December 2026
Brno hub opens; validation master plan issued

M4 September 2027
Salt Lake City exit complete


M5 June 2028
Tuttlingen exit complete

M6 December 2028
Full $103m run-rate; programme closes

Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

OPERATING MODEL | 2028

Five new units and two fewer layers cut G&A from 11.6% to 9.4% of revenue

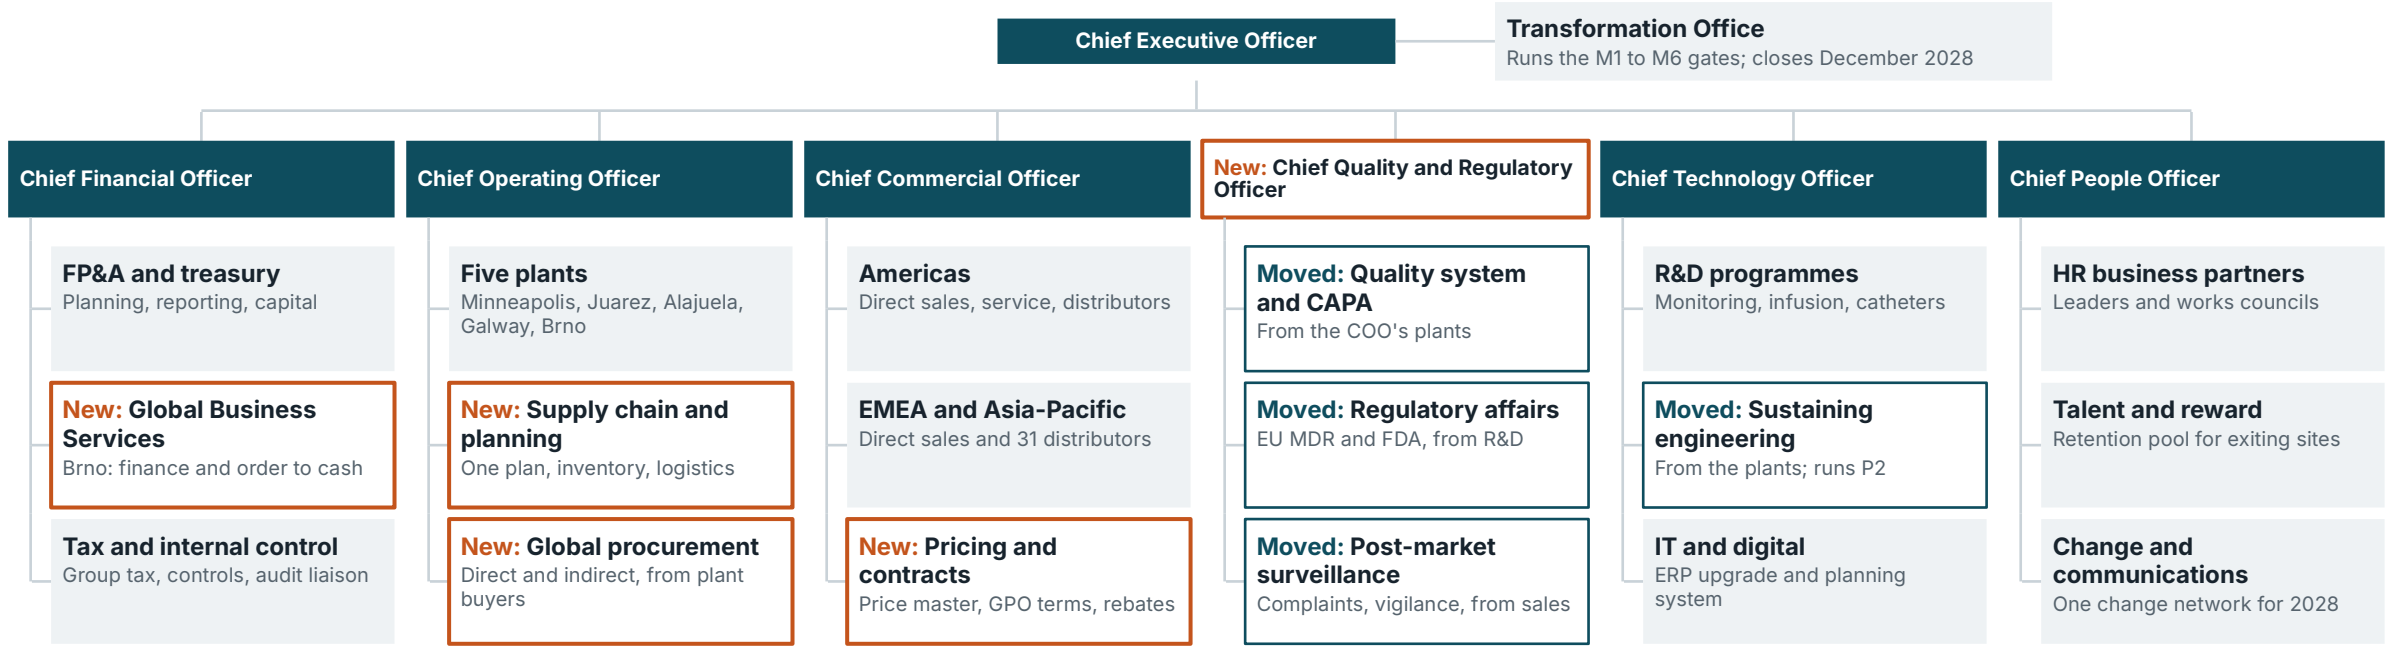

Orange outline: new, five in all, counting the quality and regulatory function; petrol outline: moved from another function; grey: unchanged; the Transformation Office closes in December 2028

Three design principles

1. One owner per process end to end: order to cash sits in the Brno hub, not in fourteen countries.
2. Quality and regulatory report to the CEO, independent of the plants they audit.
3. Plants make; procurement, planning and engineering serve all five plants.

Layers, spans and G&A cost

Measure	FY2025	FY2028
Management layers, CEO to front line	9	**7**
Average span of control	4.8	**7.0**
G&A headcount	1,180	**990**
Back-office locations	14	**3**
G&A cost ($m)	143.8	**136.3**
G&A cost, % of revenue	11.6	**9.4**

Governance to December 2028


Forum	Chair	Meets	Decides
Board	Chair	Quarterly	Passes gates M1 to M6
Transformation committee	CEO	Monthly	Scope, budget and sequence
Transformation Office	Director	Weekly	Plans, risks and benefit tracking
Benefit review	CFO	Monthly	What enters the run-rate

Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.

Mitigation brings all nine risks to ALARP or below; the two worst come from line transfers

Nine risks, before and after mitigation

Likelihood 1 rare to 5 frequent; severity 1 negligible to 5 catastrophic; score is the product

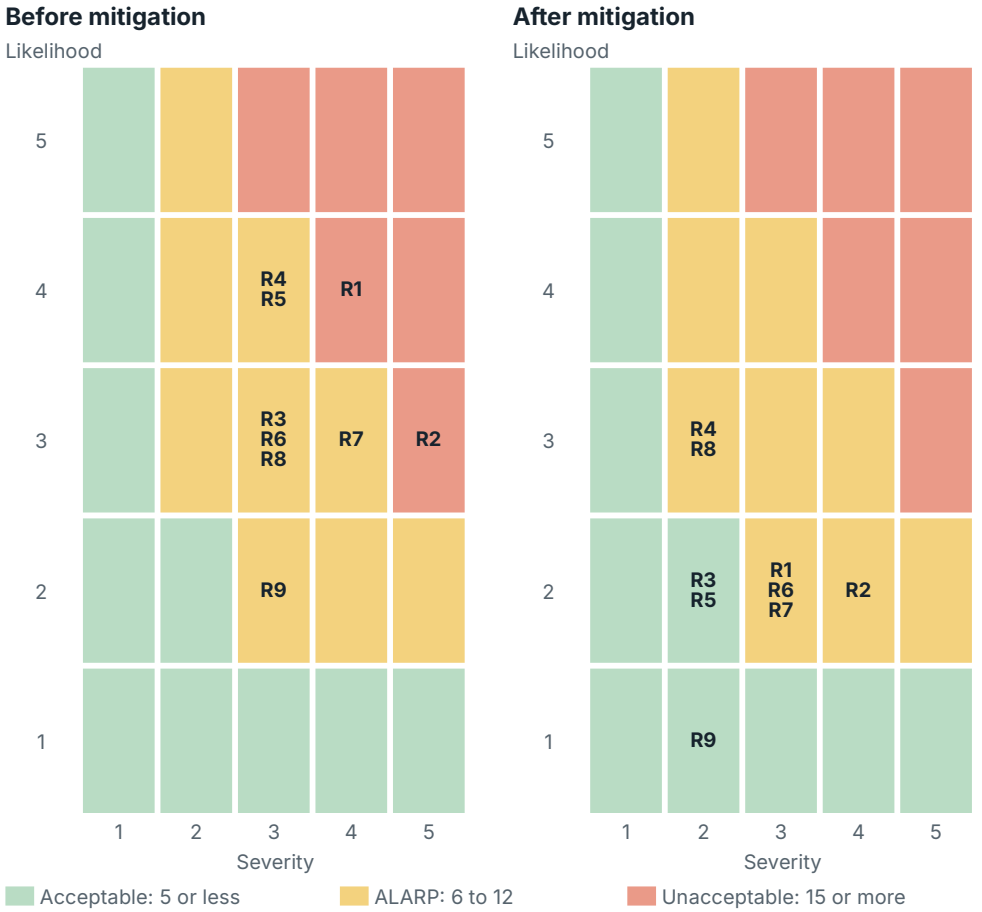

R1 and R2 come from moving validated lines. Bridge stock, build-ahead and dual qualification cut their likelihood; severity stays high because a supply gap reaches patients.

Risk register

Mitigation costs $14m in all, inside the $165m; scores before and after mitigation, shaded by zone; owners report monthly

ID	Risk	Owner	Mitigation	Cost, $m	Before	After
R1	Line re-validation delays the Salt Lake City exit	COO, CQRO	Validation master plan per line; 10 weeks of bridge stock	2.6	16	6
R2	US hospital supply interrupted during line moves	COO	12-week build-ahead; lines dual-qualified before cut-over	3.8	15	8
R3	GPO renegotiation delays price-master benefits	CCO	Phase by contract renewal date; leakage tracked monthly	0.4	9	4
R4	Order-management upgrade overruns	CFO	Upgrade the current ERP in place; no big-bang replacement	1.5	12	6
R5	Key staff leave the two closing plants early	CPO	$4.2m retention pool; knowledge transfer signed off per line	4.2	12	4
R6	Works-council consultation extends the German exit	CPO	Consultation opens Q1 2027 with 4 months of float	0.6	9	6
R7	EU MDR recertification collides with transfers	CQRO	One regulatory calendar; notified-body slots booked for 2027	0.9	12	6
R8	Inflation runs above the $31m in the plan	CFO	Index clauses in 70% of supply contracts by 2027	-	9	6
R9	Change fatigue lowers sales productivity	CCO	Commercial roles change once, in a single wave	0.3	6	2

Risks by zone

Count of risks, and their scores summed

Zone	Before	After
Unacceptable	2	0
ALARP	7	6
Acceptable	0	3
Sum of scores	100	48

What the board will see before a risk lands

Indicators reported monthly by the Transformation Office; a trigger escalates the risk out of cycle

ID	Early-warning indicator	Trigger	Escalates to
R1	Validation deviations per moved line	More than 2 open per line	Board, next meeting
R2	US service level, moved product families	Under 95% for 2 weeks	CEO within 48 hours
R3	Contracts repriced to the renewal plan	Under 80% of plan	CCO and CFO
R4	Upgrade sprints closed to plan	Under 80% in a quarter	Audit committee
R5	Regretted leavers at the closing plants	More than 5 in a quarter	CEO and CPO
R6	Works-council dates met as agreed	Any date 4 weeks late	CEO and CPO
R7	Notified-body slots confirmed for 2027	Under 3 confirmed by June	CQRO and CEO
R8	Supplier price index against the plan	Above plan two quarters	Audit committee

Source: Corrin Medical management accounts and transformation plan; FY2025 is eleven months actual and a December forecast. All figures are illustrative, invented for a fictional company.
